


# Review of the Schedule for Fuel Retrieval from SFP

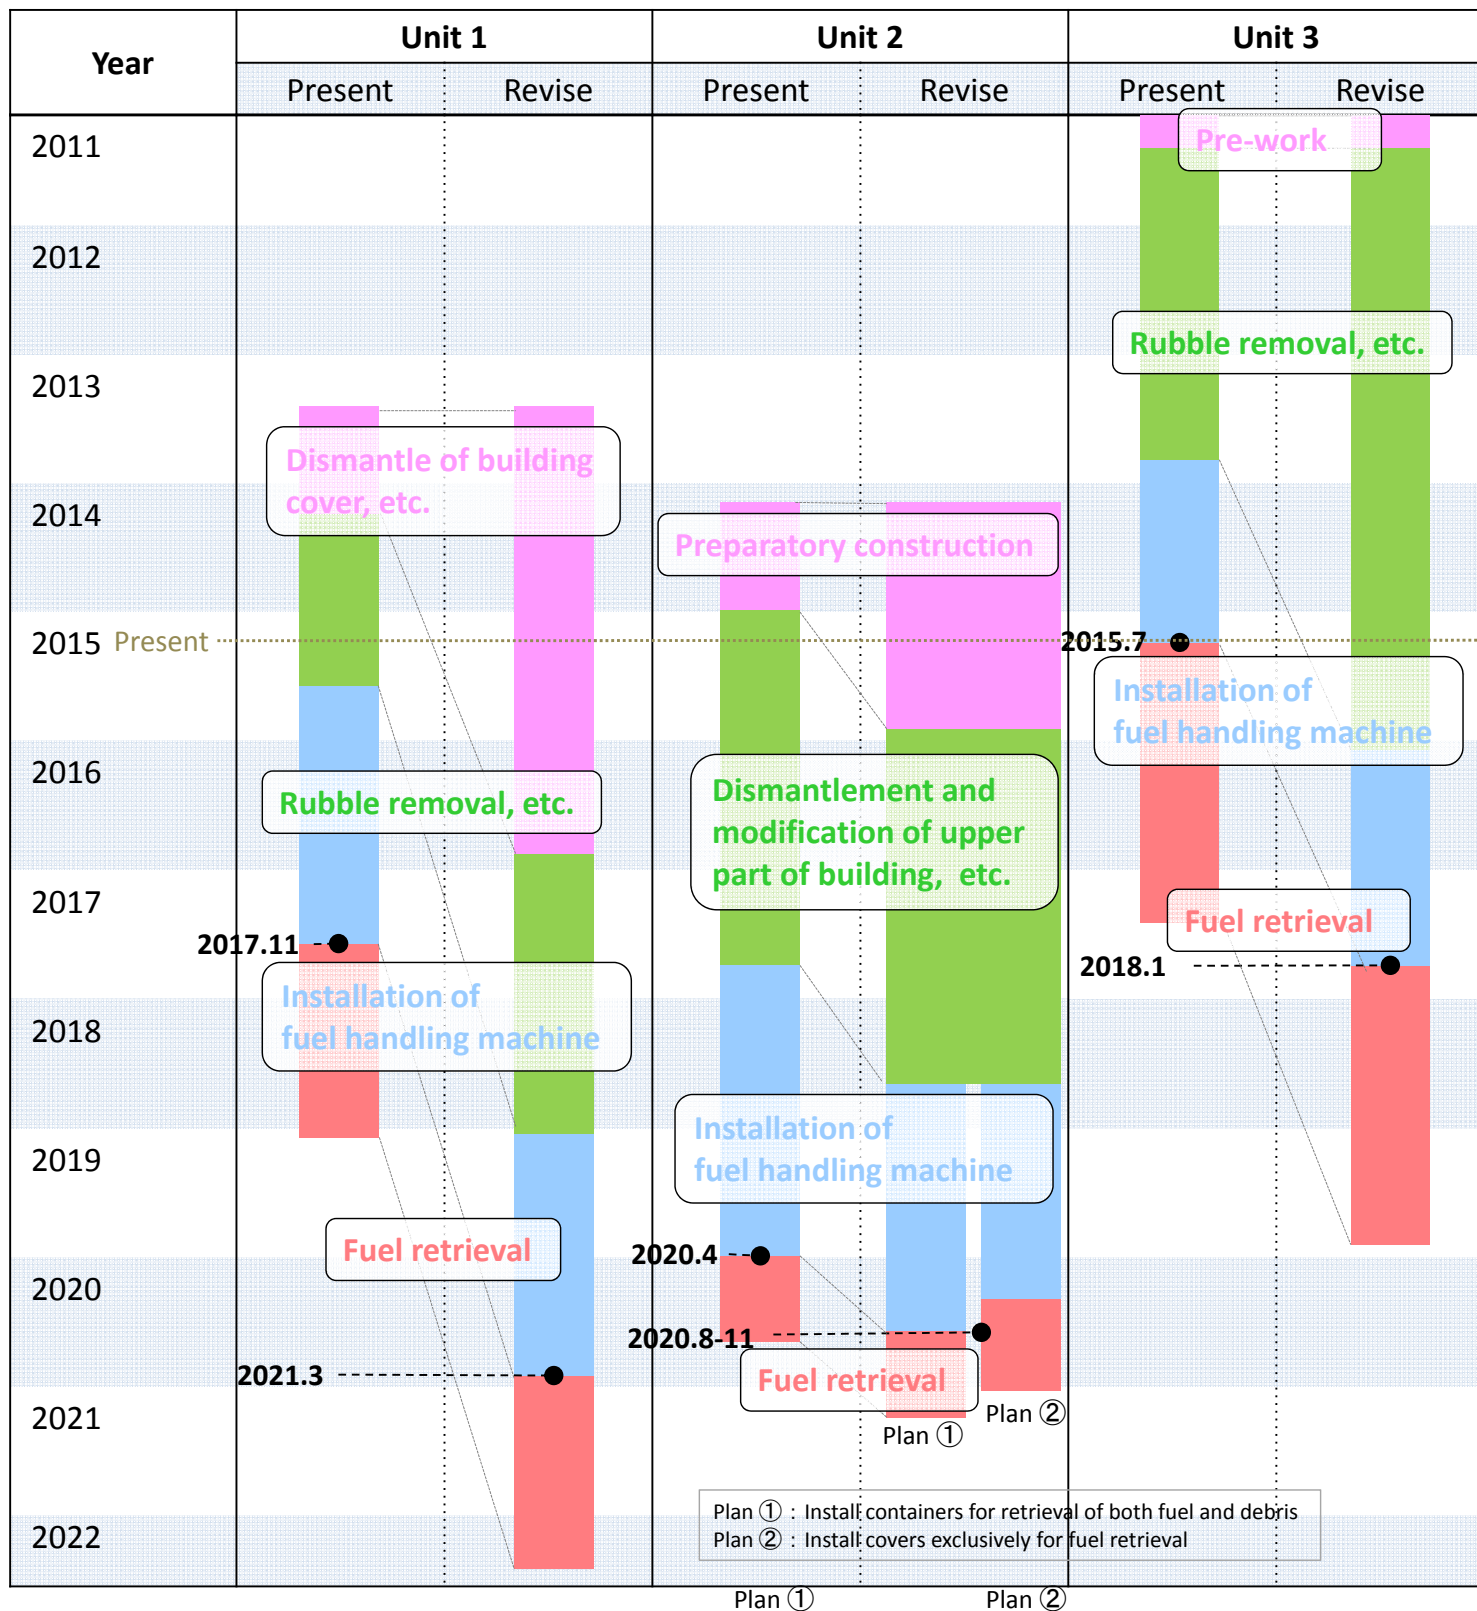

A	Additional measures for safety and securing more	+About 17.5months ex. Prevention measures for dust dispersion, etc. (+12months)	+About 3months •Review of the schedule for interference objectives removal		+About 16months ex. Additional measures for dose reduction (+14months)
B	Additional measures for identified situations	+About 13months ex. Rescheduling based on experience at Unit-3 (+10months)	+About 0.5months ex. Rescheduling based on experience at Unit-3	-About 2.5months ex. Change in fuel handling machine	+About 3months ex. Additional investigation into pool gates (+1.5months)
C	Interruption due to interference of multiple works	+About 4.5months •Schedule adjustment with land-side impermeable walls construction	+About 2months •Schedule adjustment with muon equipment installation		-
<b>Subtotal</b>		<b>+About 35months</b>	<b>+About 5.5months</b>	<b>+About 3.5months</b>	<b>+About 19months</b>
D	Troubles, such as failure in equipment, etc.	+About 5.5months ex. Failure in a crane, etc. (+3months)	-		+About 11months ex. Fall of equipment in the pool, etc. (+7months)
E	Delay in decision due to insufficient information	-	+About 1.5months •Review of building structures removal plan		-
<b>Subtotal</b>		<b>+About 5.5months</b>	<b>+About 1.5months</b>		<b>+About 11months</b>
<b>Total</b>		<b>+About 40.5months</b>	<b>+About 7months</b>	<b>+About 4months</b>	<b>+About 30months</b>
