

1号機飛散防止剤散布実績及び連続ダストモニタ計測値

2025年3月27日



東京電力ホールディングス株式会社

1.定期散布（1号機）

定期散布

目 的

オペレーティングフロア（以下、オペフロ）上へ飛散防止剤を定期的に散布し、ダストの飛散抑制効果を保持させることを目的とする。

頻 度

1回/月

標準散布量

1.5L/m²以上

濃 度

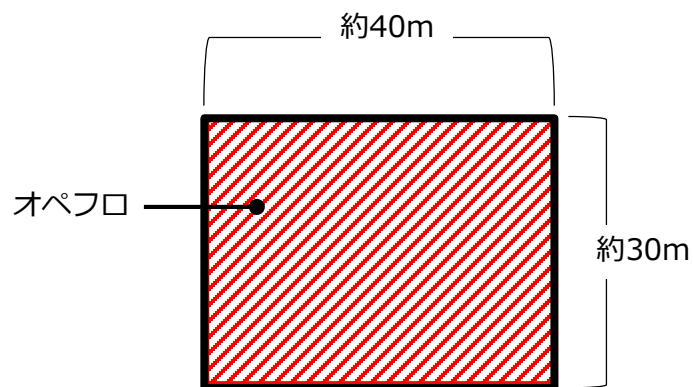
1/10

散布範囲



【凡例】

 : 散布範囲

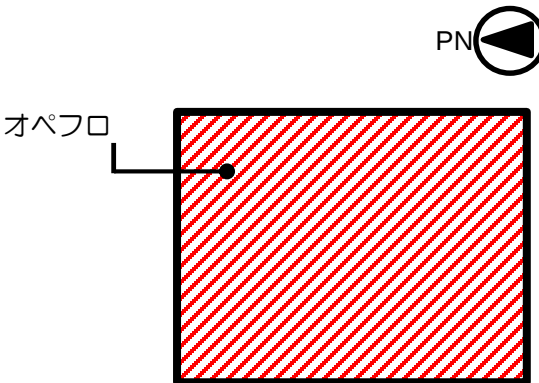
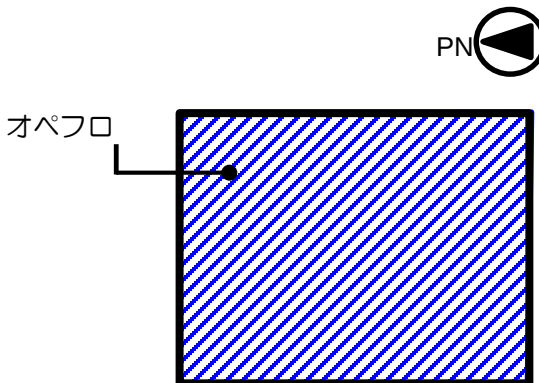
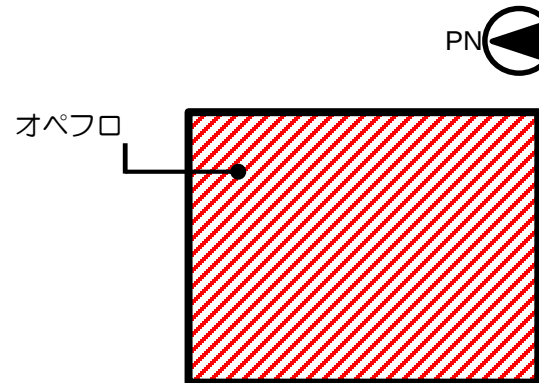


散布面積

1,234m²

2.作業時散布・定期散布の実績及び予定（1号機）

作業時散布			
目 的	オペフロ上での（ガレキ撤去や除染等）作業に応じて、飛散防止剤を散布し、ダストの飛散を抑制することを目的とする。		
標準散布量	1.5L/m ² 以上	濃 度	1/10
散布対象 作業	ガレキ撤去		

定期散布の実績及び予定		
計画（3月）	実績（3月）	計画（4月）
完了予定日：3月 4日  Map showing the planned distribution area for March. A red hatched rectangle represents the area. A point labeled 'オペフロ' (Operator Floor) is marked on the left side. A circular icon with 'PN' and a triangle is in the top right corner.	完了日：3月 4日  Map showing the actual distribution area for March. A blue hatched rectangle represents the area. A point labeled 'オペフロ' (Operator Floor) is marked on the left side. A circular icon with 'PN' and a triangle is in the top right corner.	完了予定日：4月 4日  Map showing the planned distribution area for April. A red hatched rectangle represents the area. A point labeled 'オペフロ' (Operator Floor) is marked on the left side. A circular icon with 'PN' and a triangle is in the top right corner.

【凡例】 ：計画散布範囲 ：実績散布範囲

2025年3月27日時点

3.作業時散布の実績及び予定（1号機）

2月	月	16（日）	17（月）	18（火）	19（水）	20（木）	21（金）	22（土）
	散布対象作業	－	－	－	－	－	－	－
	散布予定	－	－	－	－	－	－	－
	散布実施	－	－	－	－	－	－	－
	連続ダストモニタの計測値（Bq/cm3）※2	2.58E-04（最大）	2.13E-04（最大）	2.09E-04（最大）	2.09E-04（最大）	2.25E-04（最大）	2.13E-04（最大）	2.10E-04（最大）
		ND（最小）	9.34E-07（最小）	7.41E-07（最小）	ND（最小）	ND（最小）	ND（最小）	6.47E-07（最小）
	月	23（日）	24（月）	25（火）	26（水）	27（木）	28（金）	1（土）
	散布対象作業	－	－	－	－	－	－	－
	散布予定	－	－	－	－	－	－	－
	散布実施	－	－	－	－	－	－	－
連続ダストモニタの計測値（Bq/cm3）※2	2.25E-04（最大）	2.00E-04（最大）	2.31E-04（最大）	2.33E-04（最大）	2.00E-04（最大）	2.24E-04（最大）	2.19E-04（最大）	
	ND（最小）	ND（最小）	ND（最小）	ND（最小）	ND（最小）	ND（最小）	9.70E-07（最小）	
3月	火	2（日）	3（月）	4（火）	5（水）	6（木）	7（金）	8（土）
	散布対象作業	－	－	－	－	－	－	－
	散布予定	－	－	○	－	－	－	－
	散布実施	－	－	○	－	－	－	－
	連続ダストモニタの計測値（Bq/cm3）※3	2.34E-04（最大）	2.00E-04（最大）	2.34E-04（最大）	2.18E-04（最大）	2.12E-04（最大）	2.03E-04（最大）	2.09E-04（最大）
		7.62E-07（最小）	ND（最小）	ND（最小）	ND（最小）	ND（最小）	ND（最小）	ND（最小）
	火	9（日）	10（月）	11（火）	12（水）	13（木）	14（金）	15（土）
	散布対象作業	－	－	－	－	－	－	－
	散布予定	－	－	－	－	－	－	－
	散布実施	－	－	－	－	－	－	－
	連続ダストモニタの計測値（Bq/cm3）※3	2.36E-04（最大）	2.00E-04（最大）	2.06E-04（最大）	2.06E-04（最大）	1.82E-04（最大）	2.24E-04（最大）	2.24E-04（最大）
		7.97E-07（最小）	9.37E-07（最小）	7.56E-07（最小）	ND（最小）	ND（最小）	ND（最小）	ND（最小）
	水	16（日）	17（月）	18（火）	19（水）	20（木）	21（金）	22（土）
	散布対象作業	－	－	－	－	－	－	－
	散布予定	－	－	－	－	－	－	－
	散布実施	－	－	－	－	－	－	－
	連続ダストモニタの計測値（Bq/cm3）※4	2.09E-04（最大）	2.66E-04（最大）	2.12E-04（最大）	2.18E-04（最大）	1.97E-04（最大）	2.03E-04（最大）	2.21E-04（最大）
		ND（最小）	ND（最小）	ND（最小）	1.02E-06（最小）	ND（最小）	ND（最小）	1.48E-06（最小）
	木	23（日）	24（月）	25（火）	26（水）	27（木）	28（金）	29（土）
	散布対象作業	－	－	－	－	－	－	－
	散布予定	－	－	－	－	－	－	－
散布実施	－	－	－	－	－	－	－	
連続ダストモニタの計測値（Bq/cm3）※5	2.00E-04（最大）	2.03E-04（最大）	－（最大）	－（最大）	－（最大）	－（最大）	－（最大）	
	ND（最小）	ND（最小）	－（最小）	－（最小）	－（最小）	－（最小）	－（最小）	
